

# UK Government Major Projects Risk Dashboard

Cost, schedule and delivery-risk analysis using Excel, Power Query, Power Pivot and DAX

2025-26 PROJECTS

189

WHOLE-LIFE COST

£464.05bn

SCORED PROJECTS


81

CRITICAL / HIGH

62

## Portfolio overview

The workbook combines the 2024-25 and 2025-26 UK Government Major Projects datasets through Power Query, models the portfolio in Power Pivot and presents cost, duration, delivery-confidence and custom analytical-risk views through slicer-driven dashboards.

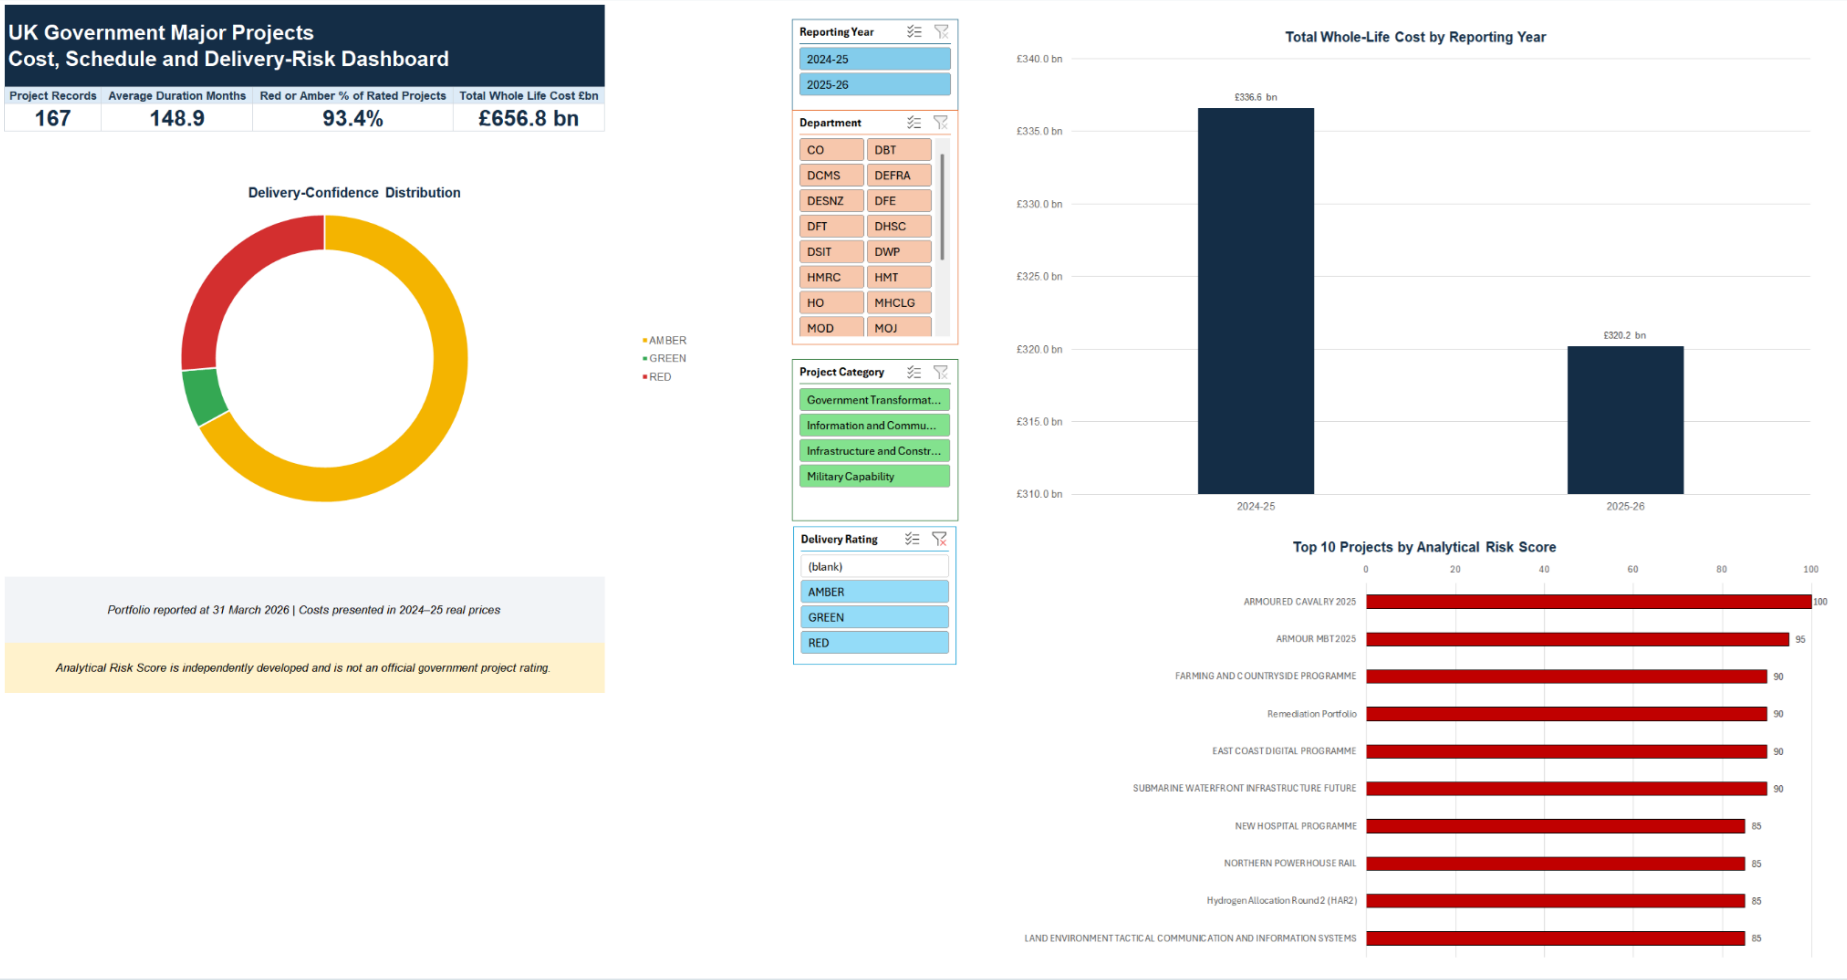

# Methodology and risk triage


The custom score is a transparent portfolio prioritisation aid - not an official NISTA, IPA or departmental rating.

## 100-point analytical risk score

- Delivery confidence: Green 5, Amber 25, Red 40 points (max 40).
- Whole-life cost exposure: banded from under £100m to £5bn+ (max 25).
- Duration exposure: banded from under 3 years to 10+ years (max 20).
- Financial-year variance: 0 to 15 points depending on variance band.
- Risk tiers: Critical 70-100, High 50-69, Medium 30-49, Low below 30; unrated projects remain Not scored.

## Cached 2025-26 finding

Of 189 projects, 81 receive an analytical score: 32 Critical, 30 High, 16 Medium and 3 Low. A further 108 projects are not scored because a usable delivery-confidence rating is unavailable. Critical-tier projects represent about £240.61bn of whole-life cost in the cached view.

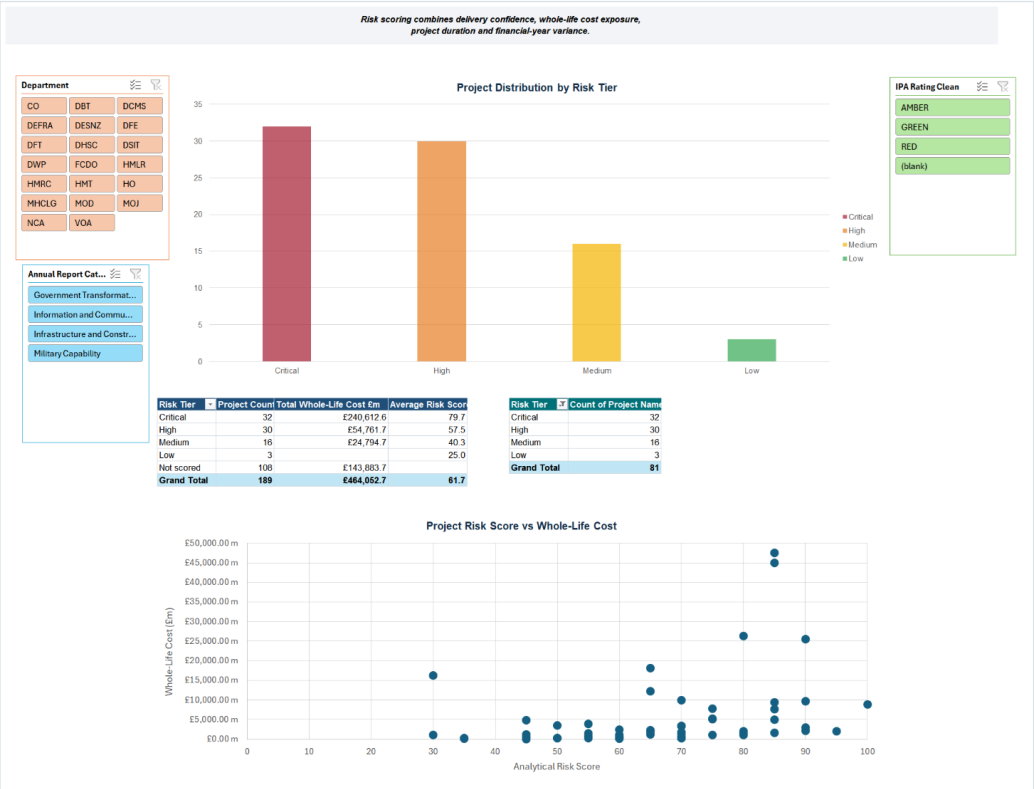

Risk Summary - tier distribution and cost exposure

# Auditability, data quality and interpretation

Review concentration and risk signals alongside missing-data coverage before drawing conclusions.

## Data quality controls

### Portfolio Validation

Confirms record counts, rating distribution and whole-life cost totals after

| Reporting Year | Count of Project Name | Sum of Whole Life Cost Clean |
|----------------|-----------------------|------------------------------|
| 2024-25        | 213                   | £565,707.28 m                |
| AMBER          | 61                    | £213,382.35 m                |
| GREEN          | 5                     | £20,339.06 m                 |
| RED            | 20                    | £102,862.12 m                |
| (blank)        | 127                   | £229,123.75 m                |
| 2025-26        | 189                   | £464,052.66 m                |
| AMBER          | 51                    | £205,226.67 m                |
| GREEN          | 6                     | £25,120.67 m                 |
| RED            | 24                    | £89,821.62 m                 |
| (blank)        | 108                   | £143,883.70 m                |
| Grand Total    | 402                   | £1,029,759.94 m              |

| Reporting Year | Project Records | Missing Cost Projects | Missing Duration Projects | Unrated Projects | Cost Data Coverage % | Duration Data Coverage % |
|----------------|-----------------|-----------------------|---------------------------|------------------|----------------------|--------------------------|
| 2024-25        | 213.00          | 56                    | 59                        | 127              | 73.7%                | 72.3%                    |
| 2025-26        | 189.00          | 56                    | 57                        | 108              | 70.4%                | 69.8%                    |
| Grand Total    | 402.00          | 112                   | 116                       | 235              | 72.1%                | 71.1%                    |

### Key controls

- Dedicated Methodology and Data Quality sheets plus a project-level risk register.
- 2025-26 cached coverage: 70.4% for whole-life cost and 69.8% for duration.
- Original source text is retained where fields include exemptions, ranges or planning-stage notes; cleaned fields are used separately for analysis.
- High cost and long duration represent exposure and complexity, not proof of poor management.

### Limitations

- Financial-year variance is not the same as whole-life cost overrun.
- Projects without usable delivery-confidence ratings remain unscored.
- Missing dates reduce schedule-analysis coverage.
- Year-to-year movement can reflect projects entering or leaving the portfolio as well as genuine project change.
